



## OIL METRIC DASHBOARD

# User eXperience Specification

Created by: Samita Bhandary

Dated: 14 Nov, 2013



## Trade Blotter ▾

Delivery Lead: Vinay Narula  
Email ID: vinay\_narula@infosys.com


Phone No: 0000000000

Settings ▾

Cummulative Chart



Velocity Chart

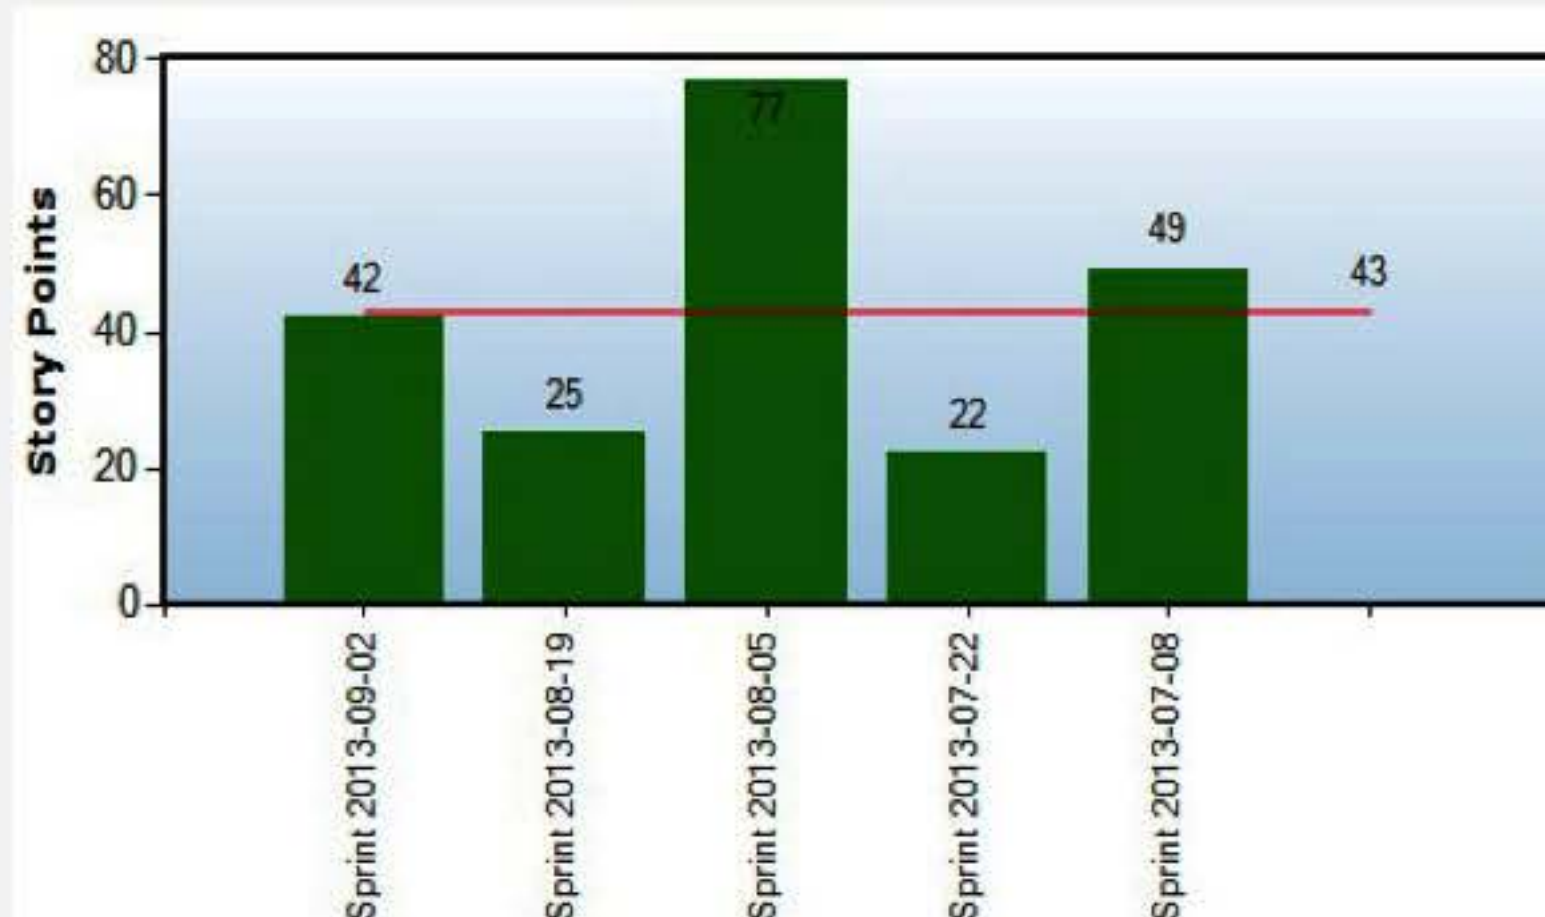

Release Information



Live Release: 10  
Automated Deployment: Yes

	Release Name	Go Live Date	No of Sprints
▶	<a href="#">Release 1</a>	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2
▶	Release 2	dd/mm/yyyy	2


Sprint Information



Release: 1

	Sprint Name	Description	Start Date	Start Date	Status
▼	<a href="#">SP11111</a>	About sprint	dd/mm/yyyy	dd/mm/yyyy	Done

PBIs Completed

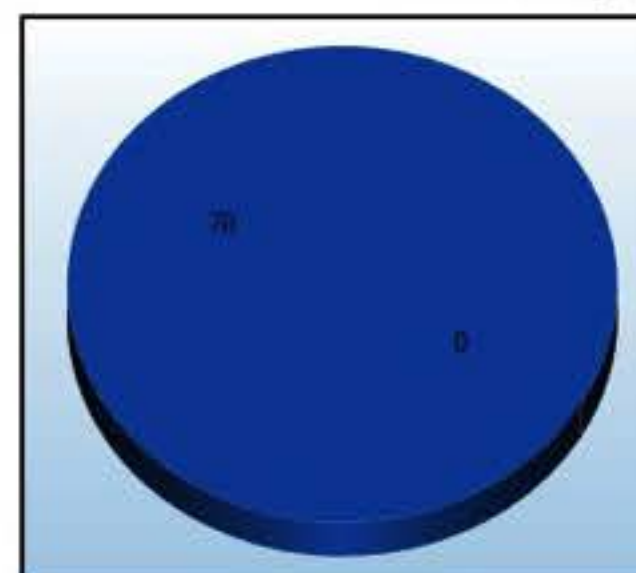


Story Points Not Completed  
Story Points Completed

▶	SP11111	About sprint	dd/mm/yyyy	dd/mm/yyyy	Done
---	---------	--------------	------------	------------	------

Additional Information

[History](#)



Metric Parameter	Project Value	Industry Standard
Unit testcoverage	00.00%	00.00%

Blockers



Title	Iteration
Change Project references	Trade Blotter

# WIREFRAME - LANDING PAGE (Drop down)

OIL METRIC DASHBOARD

Tuesday 15 Oct, 2013 | User Name Project Manager

## OIL METRIC DASHBOARD

Dashboard
Configuration ▾

Settings ▾

### Trade Blotter ▾

Delivery Lead: Vinay Narula  
 Email ID: vinay\_narula@infosys.com      Phone No: 00000000000

#### Cummulative Chart

#### Release Information

Live Release: 10  
Automated Deployment: Yes

Release Name	Go Live Date	No of Sprints
▶ Release 1	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2

#### Additional Information

Metric Parameter	Project Value	Industry Standard
Unit testcoverage	00.00%	00.00%

#### Velocity Chart

#### Sprint Information

Release: 1

Sprint Name	Description	Start Date	Start Date	Status
▼ SP11111	About sprint	dd/mm/yyyy	dd/mm/yyyy	Done

#### PBIs Completed

▶ SP11111	About sprint	dd/mm/yyyy	dd/mm/yyyy	Done
-----------	--------------	------------	------------	------

#### Additional Info History

Metric Parameter	Project Value	Industry Standard
Unit testcoverage	00.00%	00.00%
Unit testcoverage	00.00%	00.00%
Unit testcoverage	00.00%	00.00%

### Trade Blotter

Delivery Lead: Vinay Narula  
Email ID: vinay\_narula@infosys.com      Phone No: 00000000000

Settings ▾

#### Cummulative Chart

#### Release Information

Live Release: 10  
Automated Deployment: Yes

Release Name	Go Live Date	No of Sprints
▶ Release 1	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2
▶ Release 2	dd/mm/yyyy	2

#### Additional Information

Metric Parameter	Project Value	Industry Standard
Unit testcoverage	00.00%	00.00%

#### Velocity Chart

#### Sprint Information

Release: 1

Sprint Name	Description	Start Date	Start Date	Status
▼ SP11111	About sprint	dd/mm/yyyy	dd/mm/yyyy	Done

#### PBIs Completed

▶ SP11111	About sprint	dd/mm/yyyy	dd/mm/yyyy	Done
-----------	--------------	------------	------------	------

#### Additional Info History

Metric Parameter	Project Value	Industry Standard
Unit testcoverage	00.00%	00.00%
Unit testcoverage	00.00%	00.00%
Unit testcoverage	00.00%	00.00%

User can manage all panels in the dashboard. They can hide the particular panel from the dashboard and again can retrieve the panel from this drop down options.

when user click on the history link from 'Additional information' panel, the History panel will appear next to that panel with previous data.  
  
And Blocker panel move to the next row...




## Trade Blotter




Delivery Lead: Vinay Narula  
Email ID: vinay\_narula@infosys.com

Phone No:00000000000

### Cummulative Chart

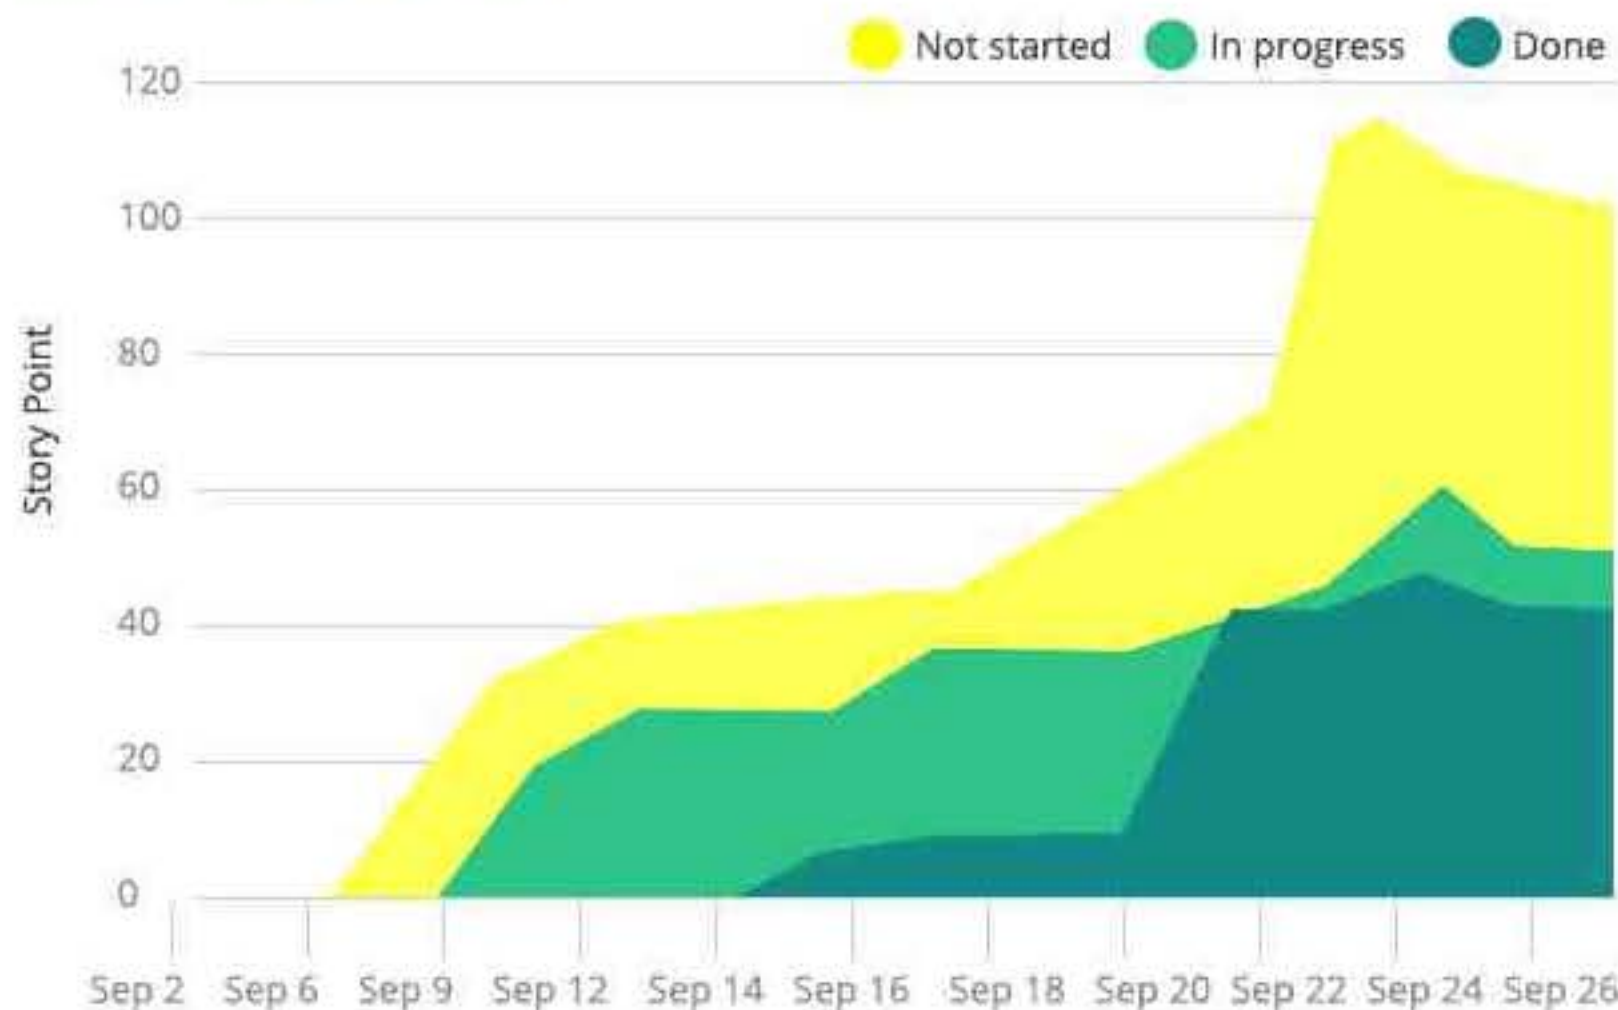

### Velocity Chart

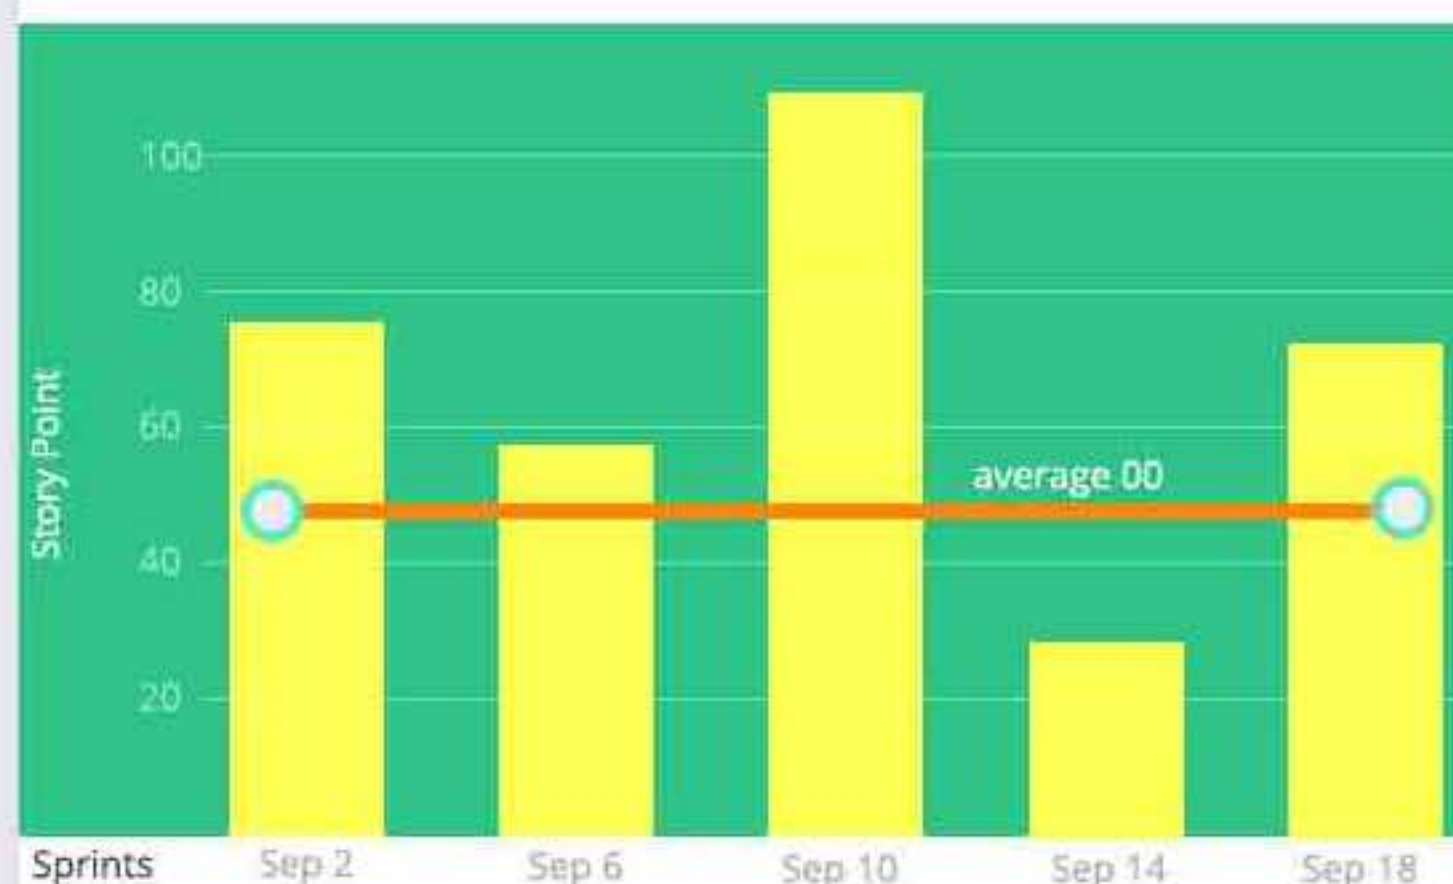

### Release information

10 Live Releases

Automated Deployment:Yes

	Release name	Go live date	Sprints
▶	Release 1	Sep 30, 2013	2
▶	Release 2	Sep 30, 2013	2
▶	Release 3	Sep 30, 2013	2
▶	Release 4	Sep 30, 2013	2
▶	Release 5	Sep 30, 2013	2

### Sprint Information

Release 1 - Sep 30, 2013



### Additional Information

History

	Metric parameter	Project value	Industry std.
	Unit test coverage	0.00%	0.00%
	Unit test coverage	0.00%	0.00%

### Blocker

	Title	Iteration
	Change Project references	Trade Blotter
	Change Project references	Trade Blotter
